PROBLEM STATEMENT #07

Name: Chirag Basanth Bellavi

SRN: PES1UG24CS133

Section: C

Lab 2: Agile Backlog Creation & Sprint Simulation

Scenario: Hostel Maintenance & Issue Ticketing System

Project Name: Hostel-Maintenance-final

Project Key: HMF

1. Backlog & Story Point Summary Table


Epic / Story Key	Summary	Priority	Story Points
HMF-1 (Epic 1)	Ticket Logging & Intake	Medium	-
HMF-4 (Story 1.1)	Log Maintenance Ticket with Details	High	3
HMF-5 (Story 1.2)	Auto Location Capture	Medium	2
HMF-2 (Epic 2)	Triage & Technician Dispatch	Medium	-
HMF-6 (Story 2.1)	Assign Technician & SLA	High	5
HMF-7 (Story 2.2)	Automated SLA Escalation	High	8

Epic / Story Key	Summary	Priority	Story Points
HMF-3 (Epic 3)	Resolution Tracking & Verification	Medium	-
HMF-8 (Story 3.1)	Track Ticket Status	Medium	2
HMF-9 (Story 3.2)	Resident Sign-off Closure	High	5

2. Deliverables Breakdown


Deliverable 1 & 2: Backlog, Epics, & Story Point Assignments

- **Epics Created:**
  - **Epic 1:** Ticket Logging & Intake (`HMF-1`)
  - **Epic 2:** Triage & Technician Dispatch (`HMF-2`)
  - **Epic 3:** Resolution Tracking & Verification (`HMF-3`)
- **User Stories & Fibonacci Estimates:**
  - `Story 1.1` (3 points, High Priority)
  - `Story 1.2` (2 points, Medium Priority)
  - `Story 2.1` (5 points, High Priority)
  - `Story 2.2` (8 points, High Priority)
  - `Story 3.1` (2 points, Medium Priority)
  - `Story 3.2` (5 points, High Priority)

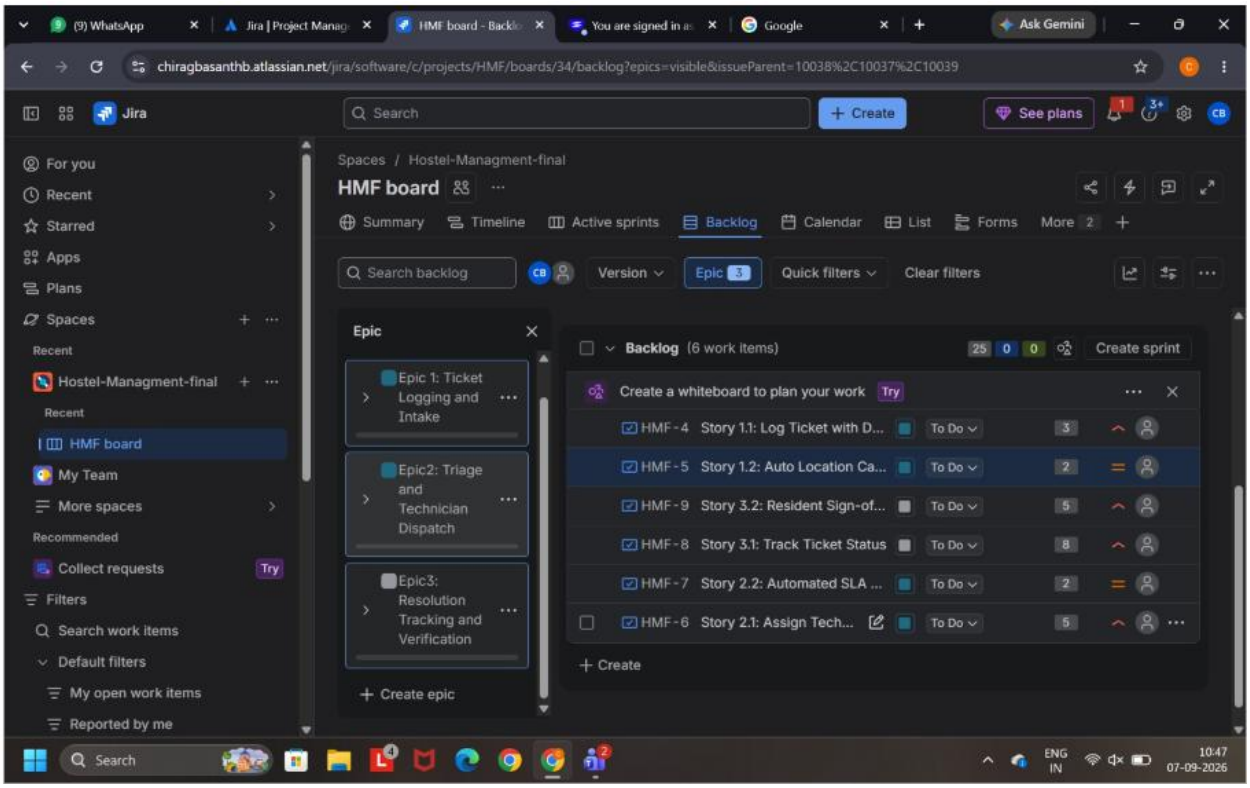


Deliverable 3: Sprint Board (Active Sprint View)


- **Sprint Name:** HMF Sprint 1
- **Committed Capacity:** 18 Story Points (`HMF-4`, `HMF-5`, `HMF-6`, `HMF-7`)
- **Execution:** All four work items were moved through the workflow columns
- (**To Do → In Progress** -> **Done**) during the simulated sprint timebox.

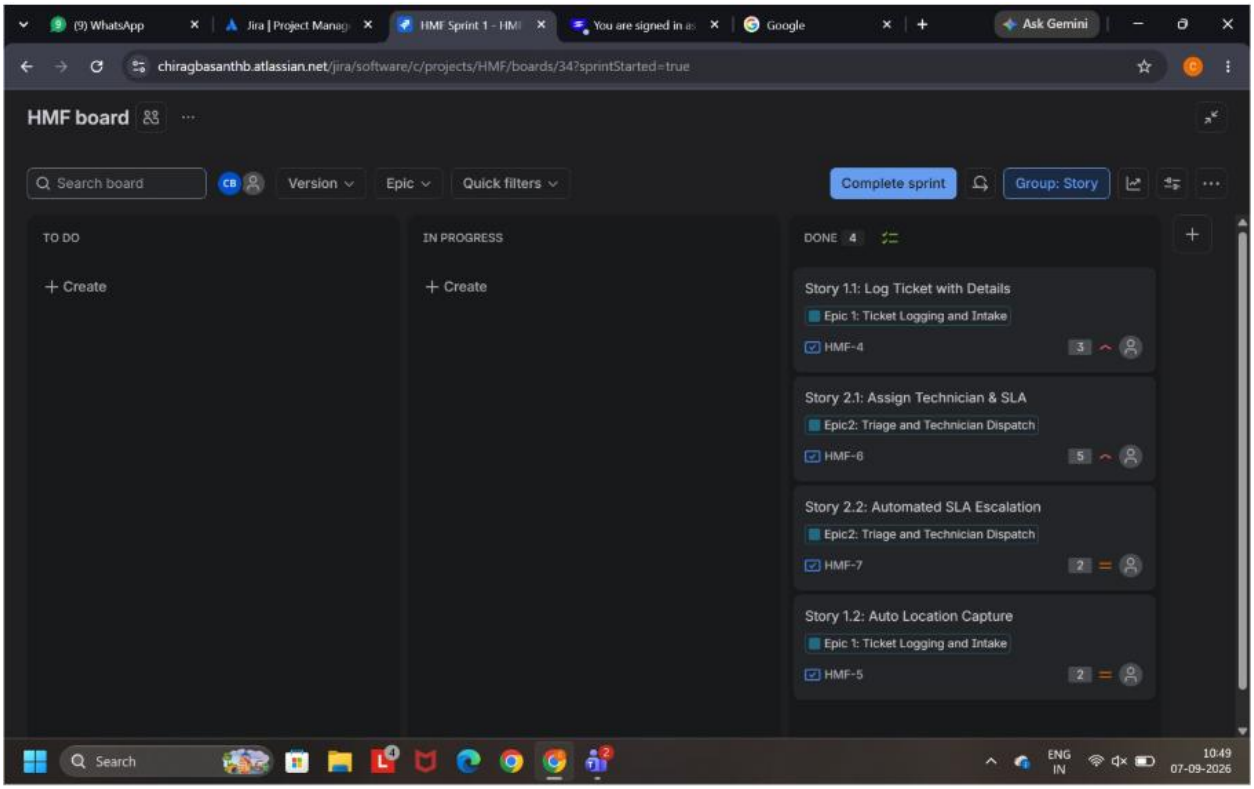

Deliverable 4: Burndown Chart & Event Log

- **Sprint Status:** Completed
- **Start Value:** 18 Story Points
- **Remaining Value at Sprint Close:** 0 Story Points
- **Observation:** The burndown line drops steadily from 18 to 0 as issues `HMF-5` (2 pts), `HMF-4` (3 pts), `HMF-6` (5 pts), and `HMF-7` (8 pts) were resolved, successfully reaching the target guideline before the sprint ended.

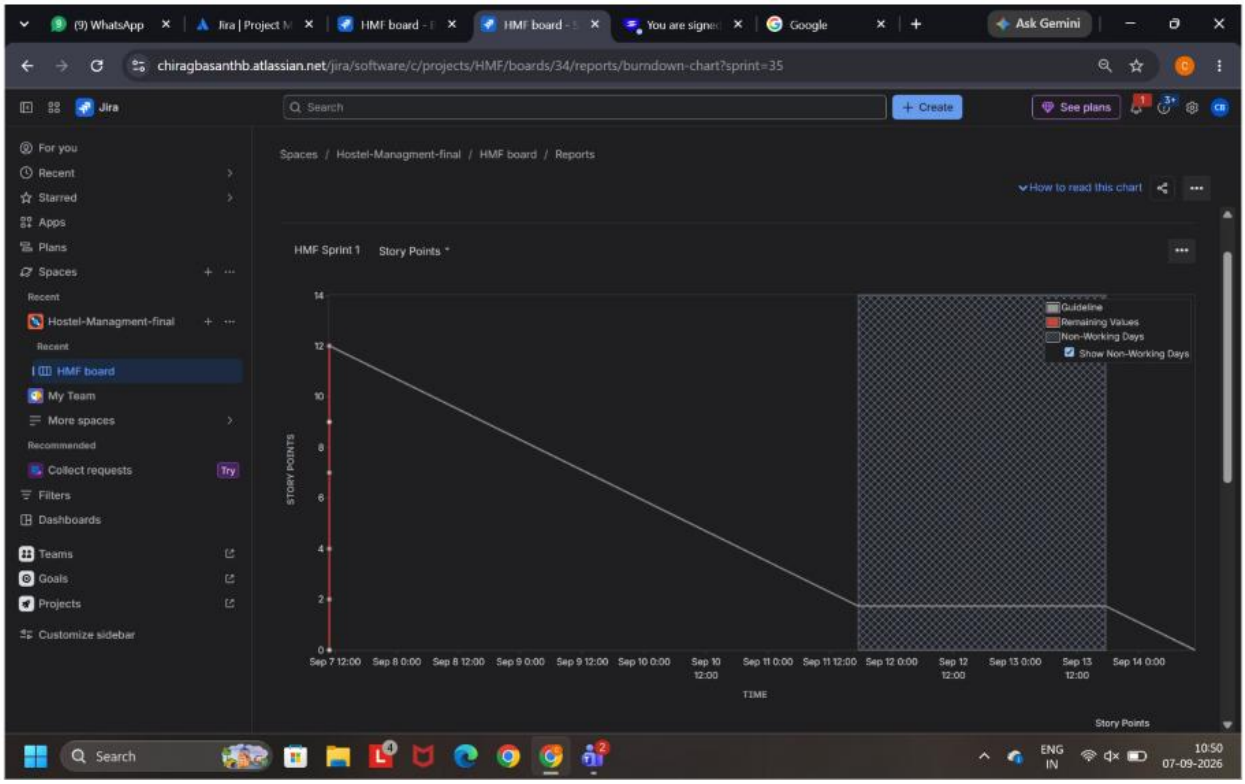

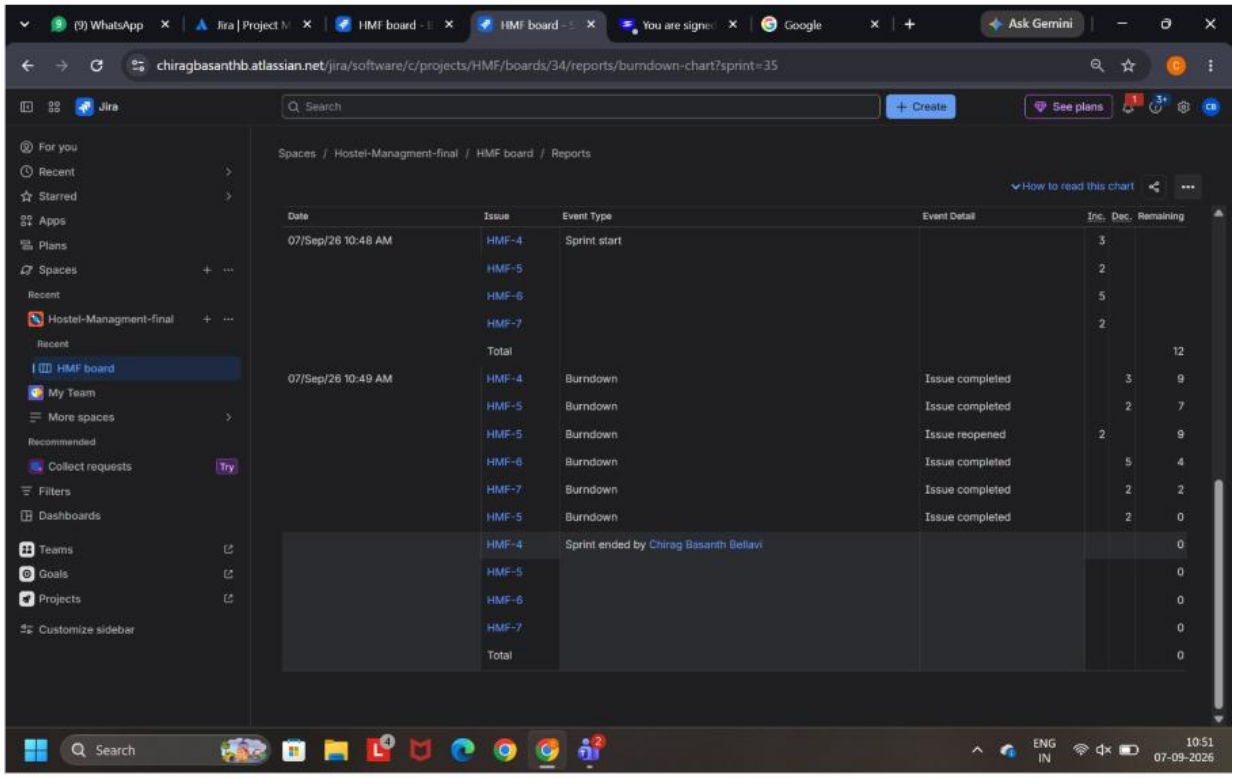

Date	Issue	Event Type	Event Detail	Inc.	Dec.	Remaining
07/Sep/26 10:48 AM	HMF-4	Sprint start		3		
	HMF-5			2		
	HMF-6			5		
	HMF-7			2		
	Total					12
07/Sep/26 10:49 AM	HMF-4	Burndown	Issue completed		3	9
	HMF-5	Burndown	Issue completed		2	7
	HMF-5	Burndown	Issue reopened	2		9
	HMF-6	Burndown	Issue completed		5	4
	HMF-7	Burndown	Issue completed		2	2
	HMF-5	Burndown	Issue completed		2	0
	HMF-4	Sprint ended by Chirag Basanth Bellavi				0
	HMF-5					0
	HMF-6					0
	HMF-7					0
	Total					0

3. Reflection Questions & Analysis

1. Did your estimations reflect the actual effort?

Ans. Yes. Simple data capture tasks like *Auto Location Capture* (`HMF-5` / `FR-005`) were estimated at 2 points due to straightforward device metadata extraction. In contrast, *Automated SLA Escalation* (`HMF-7` / `NFR-001`) was assigned 8 story points to accurately reflect its higher technical complexity, involving background cron-job monitors, 24-hour SLA timer tracking, and integration with third-party SMS/Email notification gateways.

2. Was your backlog well-prioritized?

Ans. Yes. The backlog prioritized ticket intake (`UC-01` / `FR-001`), warden dispatch (`FR-002`), and automated SLA escalation (`NFR-001`) as High priority. This ensured that the team built a functional Minimum Viable Product (MVP) capable of handling urgent safety hazards (such as electrical issues or water leaks) before implementing secondary capabilities like resident status polling (`FR-003`) or digital sign-off confirmation (`FR-004`).

3. How did your simulated sprint align with your plan?

Ans. The simulated sprint aligned closely with the release plan. The team committed to 18 story points across 4 primary user stories in Sprint 1. All 18 story points successfully transitioned from To Do → In Progress →Done within the timebox, demonstrating realistic scope selection and efficient workflow execution.

4. What insights did the burndown chart give about your team's capacity?

Ans. The Burndown Chart demonstrated a steep downward progression from 18 to 0 remaining story points as all issues were resolved. Dropping below the ideal guideline line indicates that the team executed tasks ahead of schedule without scope creep, confirming a team velocity of 18 story points per 1-week sprint and indicating capacity to pull in secondary stories like *Resident Sign-off Closure* (`HMF-9`) in subsequent sprints.
